



Commercial Proposal & Ways of Working

The cost, the timeline, and what you receive

AWNAK — Home & Family Services Platform

Itemised pricing, ways of working, the delivery schedule, the payment plan, warranty and support, change control, ownership and acceptance criteria — with an explicit line drawn between what is included and what is not.

Commercial in confidence

DOCUMENT

RAX-FIN-AWNAK-001-EN

REVISION

Rev. A

ISSUED

17 August 2026

VALID UNTIL

16 September 2026

RoboAgentix For Software Development · Doha, Qatar · roboagentix.ai · contact@roboagentix.ai · +974 3127 6894

All amounts in US dollars. Read together with RAX-TEC-AWNAK-001-EN — the Technical Proposal, which is the reference for the scope of every line in the pricing tables below.

Contents

1	Proposal summary	9	Payment plan
2	Ways of working and communication	10	Warranty and technical support
3	Delivery phases and schedule	11	Change control
4	How the work is delivered	12	Ownership, rights and confidentiality
5	Itemised pricing — phase one	13	Acceptance criteria
6	Phase two options	14	Deliverables
7	Third-party service fees	15	Assumptions and general terms
8	Out of scope	16	Next steps and approval

How to read this document

Every price line here refers to a scope described in detail in the technical document, RAX-TEC-AWWNAK-001-EN. Where the interpretation of a line's scope is in question, **the technical document governs** — not the abbreviated line title in the table.

1 Proposal summary

A proposal to deliver phase one of the **AWNAK** platform in full — a mobile app on both platforms, a backend system, an admin panel and a marketing website — at a fixed total price over a defined period, with every external integration and every phase-two item priced separately.

\$5,800 total price phase one	16 weeks delivery period	5 payments tied to milestones	180 days warranty included
15 approved screens in the customer journey	9 external integrations priced separately	17 optional items in phase two	100% code ownership to the project owner

1.1 What the total price covers

Included

- ✓ UX and interface design with a browsable interactive prototype
- ✓ Android and iOS apps from a single codebase
- ✓ Backend system, database and documented APIs
- ✓ A complete admin panel with all its modules
- ✓ Marketing website
- ✓ Nine external integrations, built and tested
- ✓ Functional, security and performance testing
- ✓ Publishing to Google Play and the App Store
- ✓ First-year hosting
- ✓ Admin training, source code and documentation handover
- ✓ 180 days of technical warranty after launch

Not included

- Third-party provider fees — messaging, maps, payment gateway, app stores **section 7**
- Everything listed as out of scope **section 8**
- Phase two items **section 6**
- Hosting beyond the first year
- Support after the warranty period **section 10**
- New changes outside the agreed scope **section 11**

The pricing principle

The price is **fixed against an agreed scope**, not open-ended by the hour. The agreed scope is what the technical document sets out, and it is finalised by signing off the requirements analysis document at the end of phase zero. Anything added after that goes through the change control process in section 11, at a rate published in advance — so there are no surprises for either party.

2 Ways of working and communication

2.1 The cadence

Iterative delivery in two-week cycles. At the end of every cycle we deliver **a build you can actually try** on the staging environment — not a report of percentage complete. That means you watch the product grow and can correct course early, rather than waiting for final delivery.

The project owner — you lead the product

You approve the design, set priorities, answer business questions, provide third-party provider accounts, and carry out acceptance testing. Your decisions determine what enters scope and what is deferred.

RoboAgentix — we build and deliver

We design, develop, test, deploy, document and train, and we guarantee that every cycle ends in a stable build you can try, and that every technical decision is explained and recorded.

2.2 Working rhythm

Activity	Frequency	Purpose
Cycle planning meeting	Every two weeks	Agreeing the next cycle's scope and ordering priorities.
Written progress report	Weekly	What was completed, what is in progress, what is blocking, and what we need from you.
Live build walkthrough	Every two weeks	Trying what has been built on staging and gathering feedback.
Shared communication channel	Daily	Quick questions and feedback — answered the same working day.
Urgent escalation	As needed	Anything blocking progress or threatening a date — answered within 4 working hours.
Phase review	End of each phase	A signed approval minute confirming what was delivered and moving the project on.

2.3 Quality gates inside each cycle

#	Gate	Effect
1	Mandatory code review	No code is merged without another developer's review — this prevents technical debt accumulating and spreads knowledge across the team.
2	Automated tests on every build	Unit and integration tests run on every push, and a failing test blocks the merge.

#	Gate	Effect
3	Dependency security scanning	Automated scanning of every external library, with critical vulnerabilities addressed before release.
4	Automatic deployment to staging	Every successful build moves to a production-equivalent environment, so you try the change running on real infrastructure.
5	Production release on your decision	Nothing reaches production without your approval, with immediate rollback to the previous release available.

3 Delivery phases and schedule

Sixteen weeks from receipt of the first payment and completion of the start-up prerequisites. Phases deliberately overlap in order to compress the timeline without sacrificing quality.

What stops the clock

The period above assumes the project owner responds within **three working days** to approval and information requests. Any delay in approvals, in providing third-party provider accounts, or in app store review **extends the schedule by the length of the delay** at no additional cost — and is recorded in the weekly progress report.

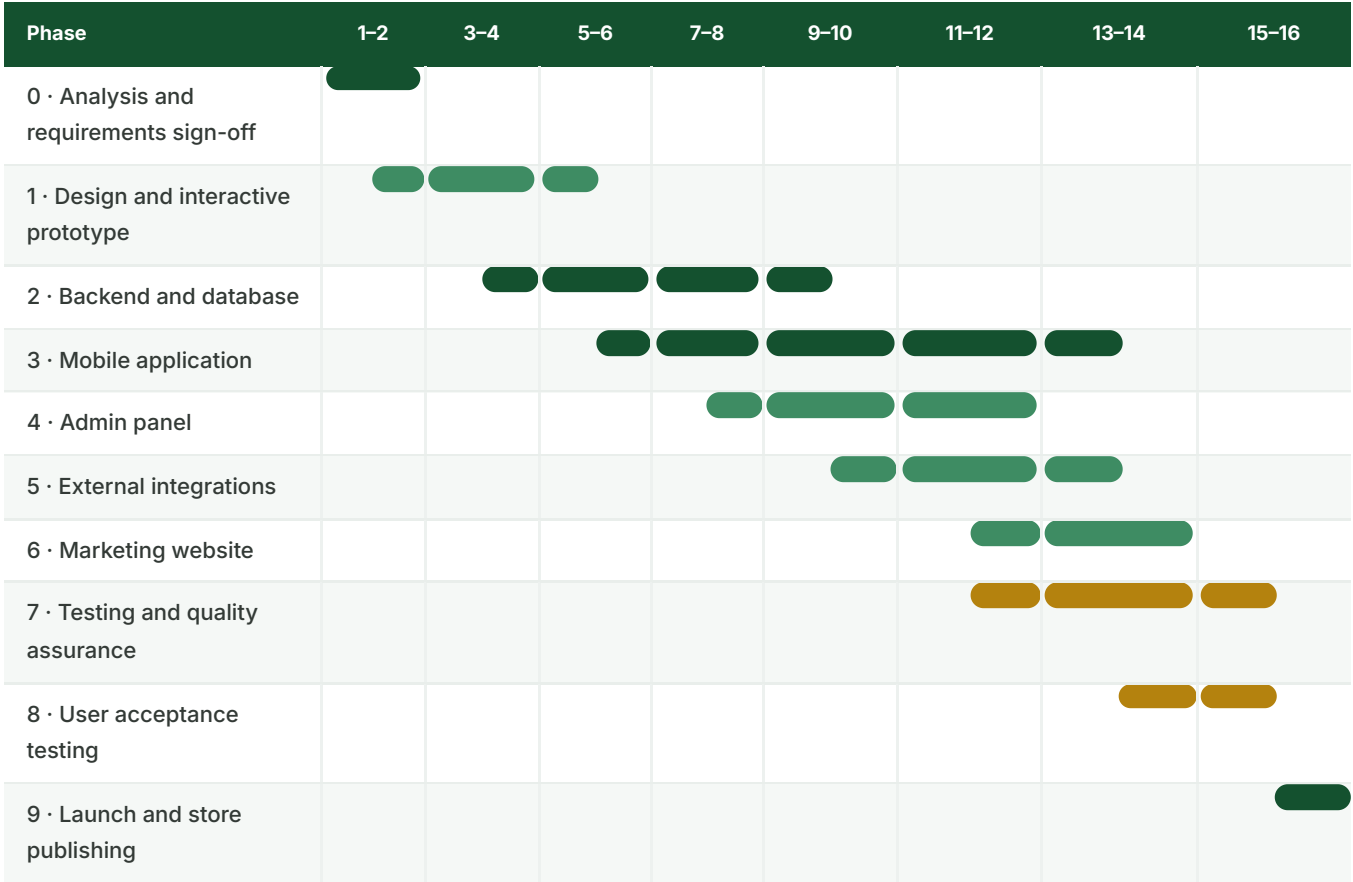


Figure 1 — Dark green marks the primary build tracks, light green the parallel tracks, and gold the testing and acceptance tracks.

3.1 Milestones and their deliverables

#	Milestone	Week	Approved deliverable
M1	Requirements sign-off	2	Final requirements document, process flow diagrams and database design.
M2	Design approval	5	An approved interactive prototype covering customer, provider and admin screens.
M3	Backend core ready	9	Documented APIs and a working database on the staging environment.
M4	Beta release	13	A testable app on both platforms covering the order cycle, plus a working admin panel.
M5	Acceptance testing passed	15	A signed UAT minute confirming the acceptance criteria in section 13 are met.
M6	Launch	16	Both apps published to the stores and the system live in production.

4 How the work is delivered

The project is delivered by a small, focused team working on an AI-assisted engineering toolchain. This is not an organisational footnote — it is **the reason for the price and the timeline** in this proposal.

A small team, single ownership

No management layers and no handoffs between teams. Whoever designs the system is who builds and delivers it, so knowledge is not lost between stages and you do not pay for internal coordination.

AI tooling in the production path

Code generation and review, test construction and documentation generation are accelerated by tools we use daily. Hours shrink without quality shrinking, because every output passes human review and automated testing.

Proven, ready components

Authentication, payments, notifications, uploads and permissions are patterns we have built before and do not rebuild from scratch. Effort concentrates on what makes Awnak distinctive: the dispatch engine, the financial layer, and the flexible service catalogue.

4.1 What this means for you

Effect	Detail
Lower cost	The price is built on the hours this toolchain actually requires, not on an agency rate card that passes ten salaries and their overheads on to you.
Shorter timeline	Sixteen weeks for a scope that conventionally takes six to nine months.
Direct communication	You speak to whoever is actually building it, not to an intermediary relaying messages. Technical decisions are taken in the same conversation.
Controlled quality	Mandatory code review, automated tests on every build, and dependency security scanning — the five gates in section 2.3 apply regardless of team size.
Guaranteed continuity	The code is documented, tested and handed over in full, and any other team can pick it up later — so there is no lock-in to us.

Disciplines covered

Business analysis · UX and interface design · mobile development · backend and database development · web front-end development · operations and deployment engineering · testing and quality assurance — all covered within the delivery team and included in the price.

5 Itemised pricing — phase one

Broken out line by line: design, the mobile app, the backend, the admin panel, the website, **the price of each external integration on its own**, testing and launch, hosting and technical support.

#	Item	Scope covered	Price (USD)
1	UX / UI design	User experience and interfaces for the customer app, provider mode, admin panel and marketing website; a complete design system; and a browsable interactive prototype.	520
2	Mobile application	A single Flutter app for Android and iOS, with customer and provider modes, every phase-one screen, RTL support, and operation on a weak connection.	1,550
3	Backend and database	Backend server, database, documented APIs, the dispatch engine, the order state machine, the financial and commission layer, messaging, notifications and permissions.	1,300
4	Admin panel	Eleven complete modules: KPIs, users, providers, orders, categories, areas, payments, complaints, content, notifications, and staff with their permissions — with reporting and export.	750
5	Marketing website	A responsive landing page managed from the admin panel, with terms, privacy, FAQ, contact form and search engine optimisation.	190
6	External integrations — each priced separately		580
6-1	OTP service integration	Phone number verification, behind an adapter that allows the provider to be swapped.	90
6-2	SMS service integration	Critical notifications by SMS.	50
6-3	Maps and geolocation integration	Location, reverse geocoding, distance and arrival time.	95
6-4	One payment gateway integration	Payment, refund and settlement behind a unified interface that accepts further gateways later.	140

#	Item	Scope covered	Price (USD)
6-5	Firebase notifications integration	Push notifications on both platforms with templates and routing.	55
6-6	Email service integration	Invoices and administrative alerts.	35
6-7	Cloud media storage integration	Uploading photos, video and documents, with compression and signed URLs.	65
6-8	Usage analytics integration	Tracking core in-app events.	25
6-9	Crash monitoring integration	Error tracking and alerting in the app and on the server.	25
7	Testing and quality assurance	Functional, integration, performance and security testing, real-device matrix testing, and support during acceptance testing.	300
8	Launch and store publishing	Preparing accounts and assets, submitting both apps, seeing review through to publication, and the production release.	130
9	Project management, analysis and documentation	Analysis, process flow diagrams, database design, technical documentation, the admin panel guide, and progress reporting.	210
10	Hosting — first year	Production and staging environments, a managed database, object storage, certificates, automated backups and monitoring.	200
11	Training and handover	Training for administrative staff, handover of the source code and accounts, and a complete backup at handover.	70
Total — phase one			\$5,800

Prices are in US dollars and exclude any taxes or bank transfer charges. The proposal is valid for thirty days from the date of issue. Item 6 is the sum of its nine sub-items, shown broken out so the price of each external integration is visible on its own.

5.1 Cost distribution across components

Component	Cost	Share	Note
Mobile application	1,550	26.7%	Largest item — two platforms from one codebase
Backend and database	1,300	22.4%	Includes the dispatch engine and the financial layer
Admin panel	750	12.9%	Eleven modules and reporting
External integrations	580	10.0%	Nine integrations
Design	520	9.0%	Four surfaces, complete interfaces
Testing and launch	430	7.4%	Includes security, performance and release
Management, analysis and documentation	210	3.6%	—
Hosting — first year	200	3.5%	Two environments
Marketing website	190	3.3%	—
Training and handover	70	1.2%	—
Total	5,800	100%	—

6 Phase two options

Entirely optional items, not included in the phase-one price. Each is priced on its own and any combination can be commissioned at any time. All have been accounted for architecturally, so none requires a rebuild.

Item	What it adds	Price	Duration
Company and team accounts	Company registration, adding technicians, distributing orders to them, staff permissions and company performance reports.	530	3 weeks
Electronic wallet	In-app balance, a transaction log, top-up and withdrawal.	385	2 weeks
Escrow hold and release	Holding the service value until completion is confirmed, with automatic settlement after commission.	365	2 weeks
Multi-city and multi-country	Currencies, time zones, and pricing and commission rules per market.	340	2 weeks
In-app calling	Voice calls between the parties without revealing phone numbers.	355	2 weeks
Technician scheduling	An appointment calendar, conflict prevention, and load distribution across technicians.	320	2 weeks
Recurring orders and maintenance plans	Weekly or monthly cleaning and maintenance subscriptions with automatic order generation.	300	2 weeks
Live provider tracking	Live location broadcast once en route, with privacy controls and automatic stop on arrival.	280	1 week
Paid subscriptions	Provider plans with display priority, lower commission and higher limits, fully managed from the panel.	265	1 week
Service guarantee	A guarantee period per service, re-ordering under guarantee, and claim tracking.	255	1 week

Item	What it adds	Price	Duration
Advanced reporting	Analytical dashboards, period-on-period comparisons and scheduled export.	250	1 week
English app interface	Enabling the English interface throughout the app, the panel and the website.	220	1 week
Loyalty programme	Points on orders, redemption as discount, and rule management from the panel.	215	1 week
Emergency services	A separate priority path, urgency surcharges, and immediate dispatch to available providers.	195	1 week
Referral programme	Referral links, rewards for both parties, and source tracking.	155	3 days
Discount codes	Codes with dates, usage limits, fixed or percentage values and scope conditions.	140	3 days
Multi-criteria ratings	Separate ratings for quality, punctuality, conduct, price and cleanliness.	130	3 days
Phase two total — if every item is commissioned		\$4,700	—

Durations are for each item in isolation; commissioning several together reduces the overall time through parallel work. Voice provider fees for in-app calling are payable by the project owner, like all other provider fees.

7 Third-party service fees

An essential clarification

These fees are **paid directly to the providers**; they do not pass through RoboAgentix and are not part of the total price. They are listed here so the financial picture is complete, as the specification requires these fees to be stated separately.

Service	Pricing model	Frequency	Note
Apple Developer account	\$99	Annual	In the project owner's name
Google Play Developer account	\$25	One-off	In the project owner's name
OTP and SMS messages	Per message	By consumption	The largest operational item — scales with registrations
Maps and geolocation	Per thousand requests	By consumption	Reduced by caching in the design
Payment gateway	Percentage per transaction	By transaction	Set by your agreement with the gateway
Email service	Monthly subscription	Monthly	Free tiers are usually sufficient at launch
Cloud storage and data transfer	By capacity and transfer	Monthly	Scales with photo and video volume
Firebase notifications	Free within standard limits	—	No cost expected in phase one
Crash monitoring and analytics	Free tiers	—	Sufficient until noticeable growth
Hosting beyond the first year	\$200	Annual	Indicative — varies with actual load

8 Out of scope

The following are **not included** in this proposal and form no part of it, in line with the specification. Any of them can be priced separately on request:

Hardware and fees

- Purchasing physical hardware or servers
- Payment gateway fees
- SMS fees
- Maps fees
- App store fees
- Hosting costs beyond the first year

Content and marketing

- Marketing photography and video
- Advertising campaigns
- Visual identity and logo design
- Professional translation
- Provider data entry

Operations and people

- Call centre
- Recruiting and field-training providers
- Provider insurance

Other systems

- Integration with an external accounting system
- Maintenance after the warranty period
- Any function not set out in the technical document

9 Payment plan

Five payments tied to **verifiable milestones**, not to dates. No payment falls due until its milestone's deliverable has been approved in writing.

#	Trigger	Milestone	Share	Amount (USD)
1	On contract signature and project start	—	25%	1,450
2	On approval of the design and interactive prototype	M2	20%	1,160
3	On delivery of the testable beta release	M4	25%	1,450
4	On passing acceptance testing and signing its minute	M5	20%	1,160
5	Thirty days after launch, once operation is stable	M6	10%	580
Total			100%	\$5,800

Each payment is settled within ten working days of the invoice date. Phase two items — if commissioned — are paid in two instalments, 50% on start and 50% on delivery, under a separate contract addendum.

10 Warranty and technical support

10.1 The included warranty period

One hundred and eighty days from the date of publication on both stores. During that period **software defects** are fixed at no charge — a defect being any behaviour that departs from the technical document and the approved requirements analysis.

Severity	Definition	Response time	Resolution time
Critical	Blocks the order cycle, halts the system, or affects the integrity of funds.	4 working hours	24 hours
High	Disables a major function while a temporary workaround exists.	1 working day	3 working days

Severity	Definition	Response time	Resolution time
Normal	Limited-impact defect or a cosmetic issue.	3 working days	10 working days

Faults are received by dedicated email and the shared communication channel, with a numbered ticket per report tracked through to closure.

10.2 What the warranty does not cover

- **New changes** and additional functionality — priced through change control.
- Changes caused by **payment, maps or app store** provider updates, or operating system updates — estimated separately.
- Faults arising from code or configuration changes made by another party after handover.
- Outage of an external provider, or exceeding that provider's account limits.
- Incorrect data entry or misuse of the admin panel.

10.3 Support after the warranty period

Package	Monthly	Hours	Includes
Basic	\$50	10	Defect fixing, monitoring, backups and security updates.
Standard	\$100	25	The above, plus small changes, store compatibility updates and priority response.
Advanced	\$180	50	The above, plus continuous development, monthly performance reports and a dedicated engineer.

Unused hours carry over for one month. Hosting renews annually at an indicative \$200 depending on actual load. These packages are optional and are not a condition of the main contract.

11 Change control

Change is normal on a project of this size. What matters is that it is never **ambiguous** — every change request follows a published path with a price known before it is carried out.

- 1

A written request

The project owner sends the change request through the agreed channel, described in enough detail to assess its impact.
- 2

An estimate within three working days

We respond with an estimate of hours, cost and schedule impact, with no commitment on your part.
- 3

Approval or rejection

No change is carried out before written approval. Rejection carries no cost.
- 4

Delivery and documentation

The change enters the appropriate cycle, and the technical document and schedule impact are formally updated.

Item	Price	Note
Development or design hour	\$8	For changes outside the agreed scope.
Small change up to 4 hours	Free	Up to 16 hours cumulatively across the project — at no charge.
Re-prioritising within scope	Free	Provided the total remains unchanged.
An additional external integration	from \$70	Depending on the provider's complexity and documentation.

12 Ownership, rights and confidentiality

An explicit undertaking

Ownership of the application, the systems and everything produced within this project rests **entirely and without reservation** with the project owner, effective on settlement of the final payment.

- ✓ **The complete source code is handed over** — server, app, admin panel, marketing website, database migration files and version history.
- ✓ **App store accounts** are created and remain in the project owner's name.
- ✓ **Hosting, domain and external service accounts** are created in the project owner's name and all access credentials are handed over in full.
- ✓ **RoboAgentix may not** resell the same system with the project's data, identity or content.
- ✓ **Customer and provider data may not be used** for any other purpose, under any circumstances.
- ✓ **Complete confidentiality** over project information during delivery and afterwards, without time limit.
- ✓ RoboAgentix may cite the project as a reference **only with prior written consent**.

RoboAgentix retains ownership of its own general-purpose internal tools and libraries that are not specific to this project, and grants the project owner a perpetual, irrevocable licence to use them within this system at no further cost — so no future obligation or dependency arises from them.

13 Acceptance criteria

The system is deemed accepted when the following twenty criteria are met — these are the acceptance criteria set out in the specification. They are executed as acceptance test scenarios with the project owner present, and signed off by minute.

#	Criterion	Status
1	Customer registers and verifies their phone number successfully	UAT
2	Provider registers and submits their documents	UAT
3	The operator approves the provider	UAT
4	The customer creates a complete order	UAT
5	The order reaches the appropriate providers	UAT
6	A quote is submitted	UAT
7	The customer accepts the quote	UAT
8	The provider begins carrying out the order	UAT
9	Order status updates correctly	UAT
10	An additional cost is added after customer approval	UAT
11	Service completion is confirmed	UAT
12	Commission is calculated correctly	UAT
13	The payment is recorded	UAT
14	The invoice is issued	UAT
15	Rating is completed	UAT
16	A complaint is opened and handled	UAT
17	Correct data appears in the admin reports	UAT
18	Notifications are delivered successfully	UAT
19	The app works on Android and iOS	UAT

#	Criterion	Status
20	No critical defects prevent the order cycle completing	UAT

The acceptance rule

The system is accepted once the twenty criteria are met. If the project owner raises no written comments within **ten working days** of the acceptance build being delivered, the deliverable is deemed accepted — protecting the schedule from open-ended suspension.

14 Deliverables

- ✓ Final requirements analysis document
 - ✓ Process flow diagrams
 - ✓ Database design
 - ✓ UX design
 - ✓ An approved interactive prototype of the app interfaces
 - ✓ Android application
 - ✓ iOS application
 - ✓ Backend system
 - ✓ Admin panel
 - ✓ Database
 - ✓ Documented APIs
 - Marketing website
- ✓ Notification integration
 - ✓ Maps integration
 - ✓ OTP integration
 - ✓ The agreed payment integration
 - ✓ Functional, security and performance testing
 - ✓ App store submissions
 - ✓ Complete source code
 - ✓ Hosting and database credentials
 - ✓ Admin panel user guide
 - ✓ Training for administrative staff
 - ✓ A backup at handover
 - ✓ Technical documentation for the system and its APIs

15 Assumptions and general terms

Item	Term
Proposal validity	Thirty days from the date of issue shown on the cover.
Currency and taxes	All amounts in US dollars, excluding any taxes or bank transfer charges.
Scope finalisation	Scope is finalised by signing off the requirements analysis document at the end of phase zero.
Scope reference	In any dispute over the interpretation of a line, the technical document RAX-TEC-AWNAK-001-EN governs.
The project owner's responsibilities	Approvals within three working days; providing third-party provider accounts, copy and logo; and nominating a single contact authorised to decide.
Provider accounts	Created in the project owner's name and at their expense; we provide technical support in setting them up at no charge.
App store review	Outside either party's control; we undertake to address any review comment promptly through to publication.
Initial data	Entering provider and operational category data is the project owner's responsibility; we hand over the system with sample categories ready to edit.
Working languages	Arabic for communication and documentation; English for code and technical documentation.
Governing law	To be set in the final contract by agreement between the parties.

16 Next steps and approval

1

Review both documents

Review the technical and commercial proposals together and send any question or scope amendment.

2

Clarification session

A meeting to discuss scope, pricing and schedule, and to settle what enters phase one and what is deferred.

3

Contract signature

The final contract is built on these two documents as binding annexes, not as indicative attachments.



Start

Receipt of the first payment and the start of phase zero within five working days of signature.

For RoboAgentix

For the project owner

Name and title · Signature · Date
RoboAgentix For Software Development — Doha, Qatar

Name and title · Signature · Date
Awnak — Home & Family Services Platform

End of the commercial document · RAX-FIN-Awnak-001-EN · Rev. A
Read together with RAX-TEC-Awnak-001-EN — the Technical Proposal
roboagentix.ai · contact@roboagentix.ai · +974 3127 6894
